


Capital Works

May Update

Infrastructure & Public Works Committee

This report provides an overview of Capital Projects either complete or progressing for the month of May 2024

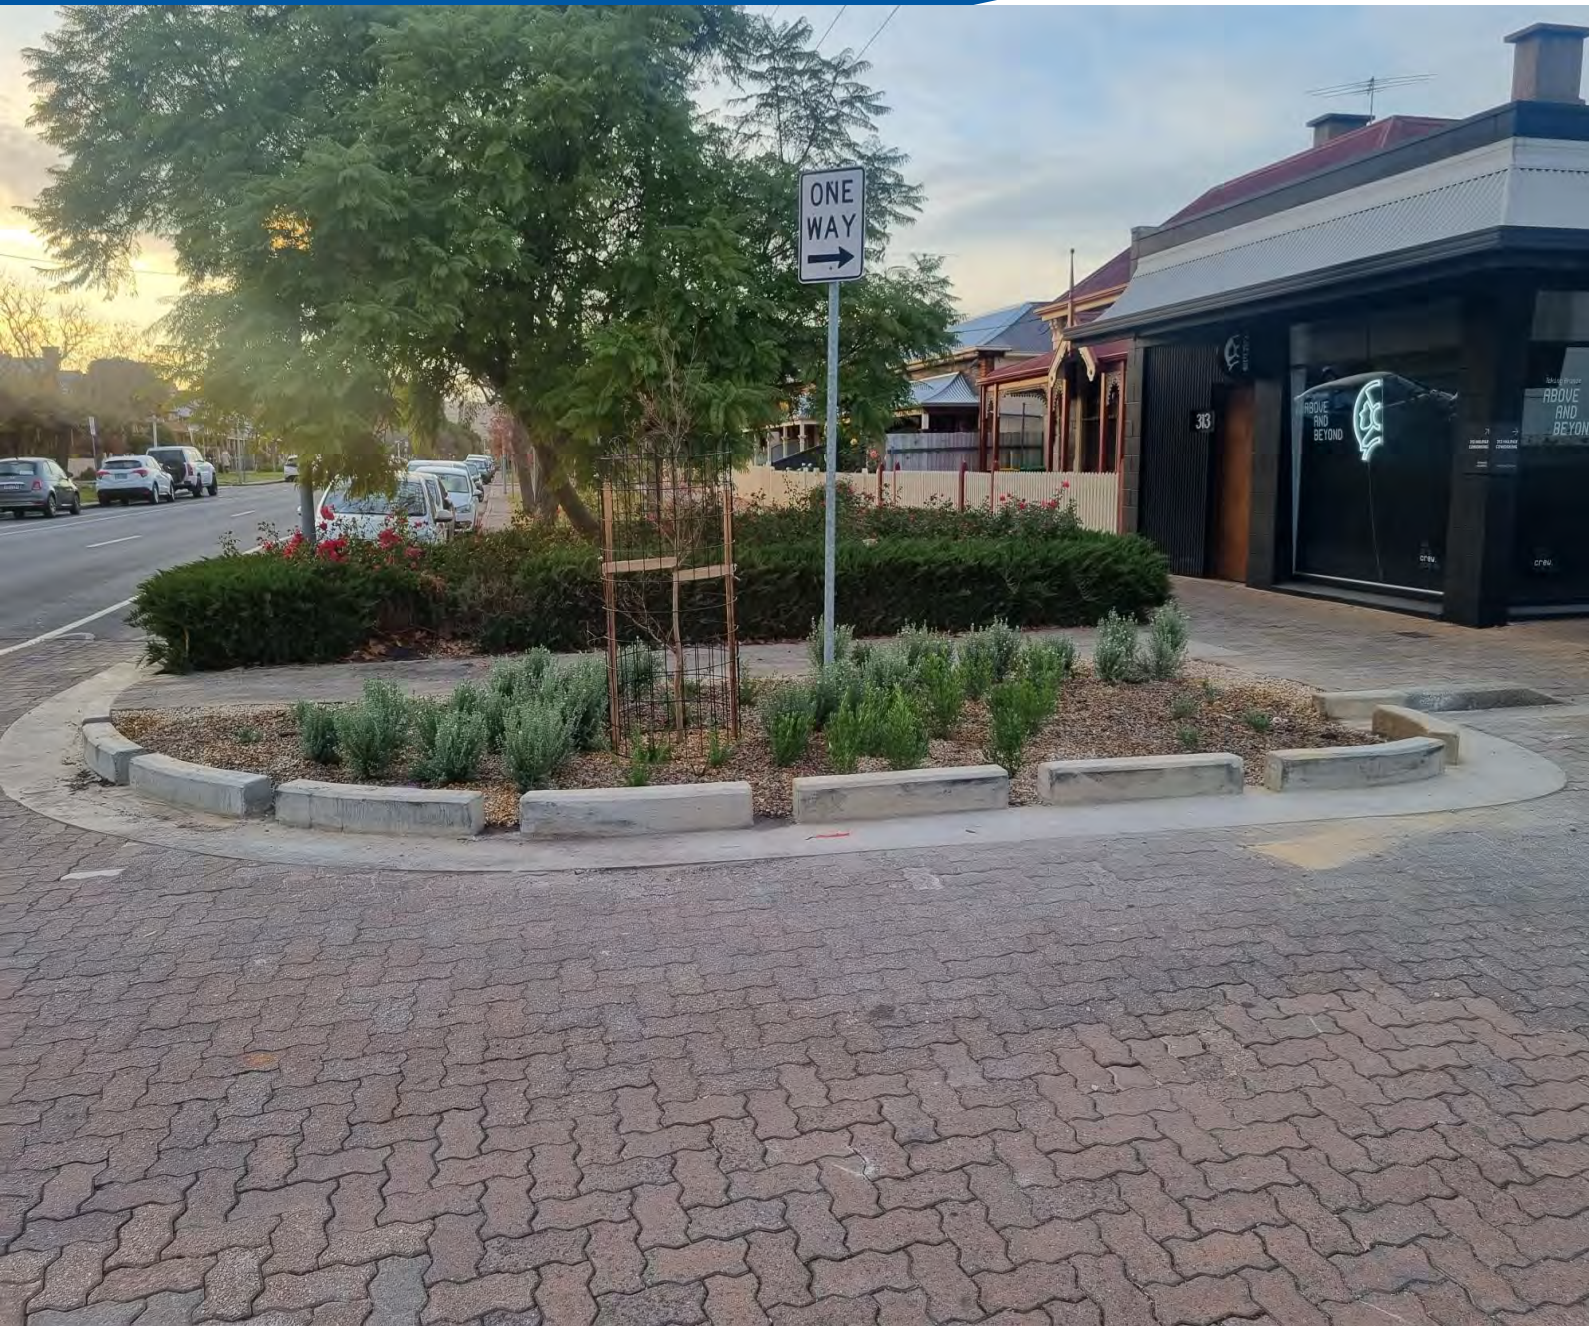

North-South Bikeways

\$5.5m

Major Project



The Contractor has made a great start along the North Terrace to Rundle Street section.

New stormwater works are progressing well and are expected to be completed in June/July 2024 with new footpaths being completed concurrently. Footpaths are expected to be complete, and usable by the public in July/August 2024.

All three sections are expected to be completed in October 2024.

Hellas Sports Club Building Lighting Mary Lee Park (Park 27B)

\$710,000

Major Project



The sports lighting enabling works such as trenching/excavation, installation of conduits, light pole footings and pits, have been completed.

Light towers are now being installed onsite.

Anticipated date for Practical Completion is the June 2024, subject to the weather.

Hutt Street Entry Statement and Auxiliary Works

\$3m (plus auxiliary works)

New/Upgrade



Construction in progress and on track for completion by November 2024.

All excavation completed, and underground services (stormwater, electrical, irrigation etc) installed. Permeable pavement on western side of Hutt Road within the Park Lands is fully completed, and approximately 30% of the exposed aggregate concrete path on the eastern side of Hutt Road is constructed.

Installation of public artwork pieces, protuberances for 14 avenue trees within the parking lane and construction of a signalised raised crossing will commence in June.

Construction works are expected to be completed in August, with planting to follow to allow the site to be opened for public ahead of schedule.

Field Street Streetscape Upgrade

\$2.4m

New/Upgrade



New stormwater system completed. With the entire Field Street now under construction including, electrical works, concreting works, light pole installation, tree cell installation and footpath construction. Ongoing stakeholder engagement with businesses being undertaken to ensure operation of businesses.

Greening City Streets Program

\$1.2m

New/Upgrade



Ada Street Greening



Ada Street Greening

Ada Street Greening Works now complete. The works involved 5 new in-ground trees and 1 large garden bed with low-level plantings.

Contractor is now progressing with works along Wyatt Street. This is the final street in the greening city streets project. Works are expected to be completed in mid-June.

Carriageway Park/Tuthangga (Park 17) Earthen Levee Stormwater Management

\$330,000

New/Upgrade



Construction commenced in late May and is on track for completion by 30 June 2024.

Approximately 30% of the levee is constructed and will continue to build the core of the levee and lay topsoil with grass cover in the month of June.

The levee will provide a first line of flood protection to the Hutt Road and South Terrace intersection.

Adelaide Town Hall Façade

\$4.96m

Renewal



King William Street Scaffold is progressing around Albert Tower.

Plastering, stabilisation, cleaning and painting are currently underway. Practical completion is expected in December 2024.

Melbourne Street Bus Stop 4 (City Bound)

Renewal



Melbourne Street Bus Stop 4 has been reinstated and is now operational.

Works included pavement alterations, line marking, and signage as well as street furniture adjustments.
