

VAILO

ADL

SOO

***CONSULTATION
PROCESS***

KADALTILLA

(Adelaide Park Lands Authority)

23 May 2024

AGENDA

Declared Area

Program Overview


Prescribed Works Period & Key Dates

Road Closures & Openings

Proposed Works / Improvements

2024 DECLARED AREA

The Declared Area has been developed to facilitate the delivery of Adelaide 500 objectives, while limiting disruption where possible.

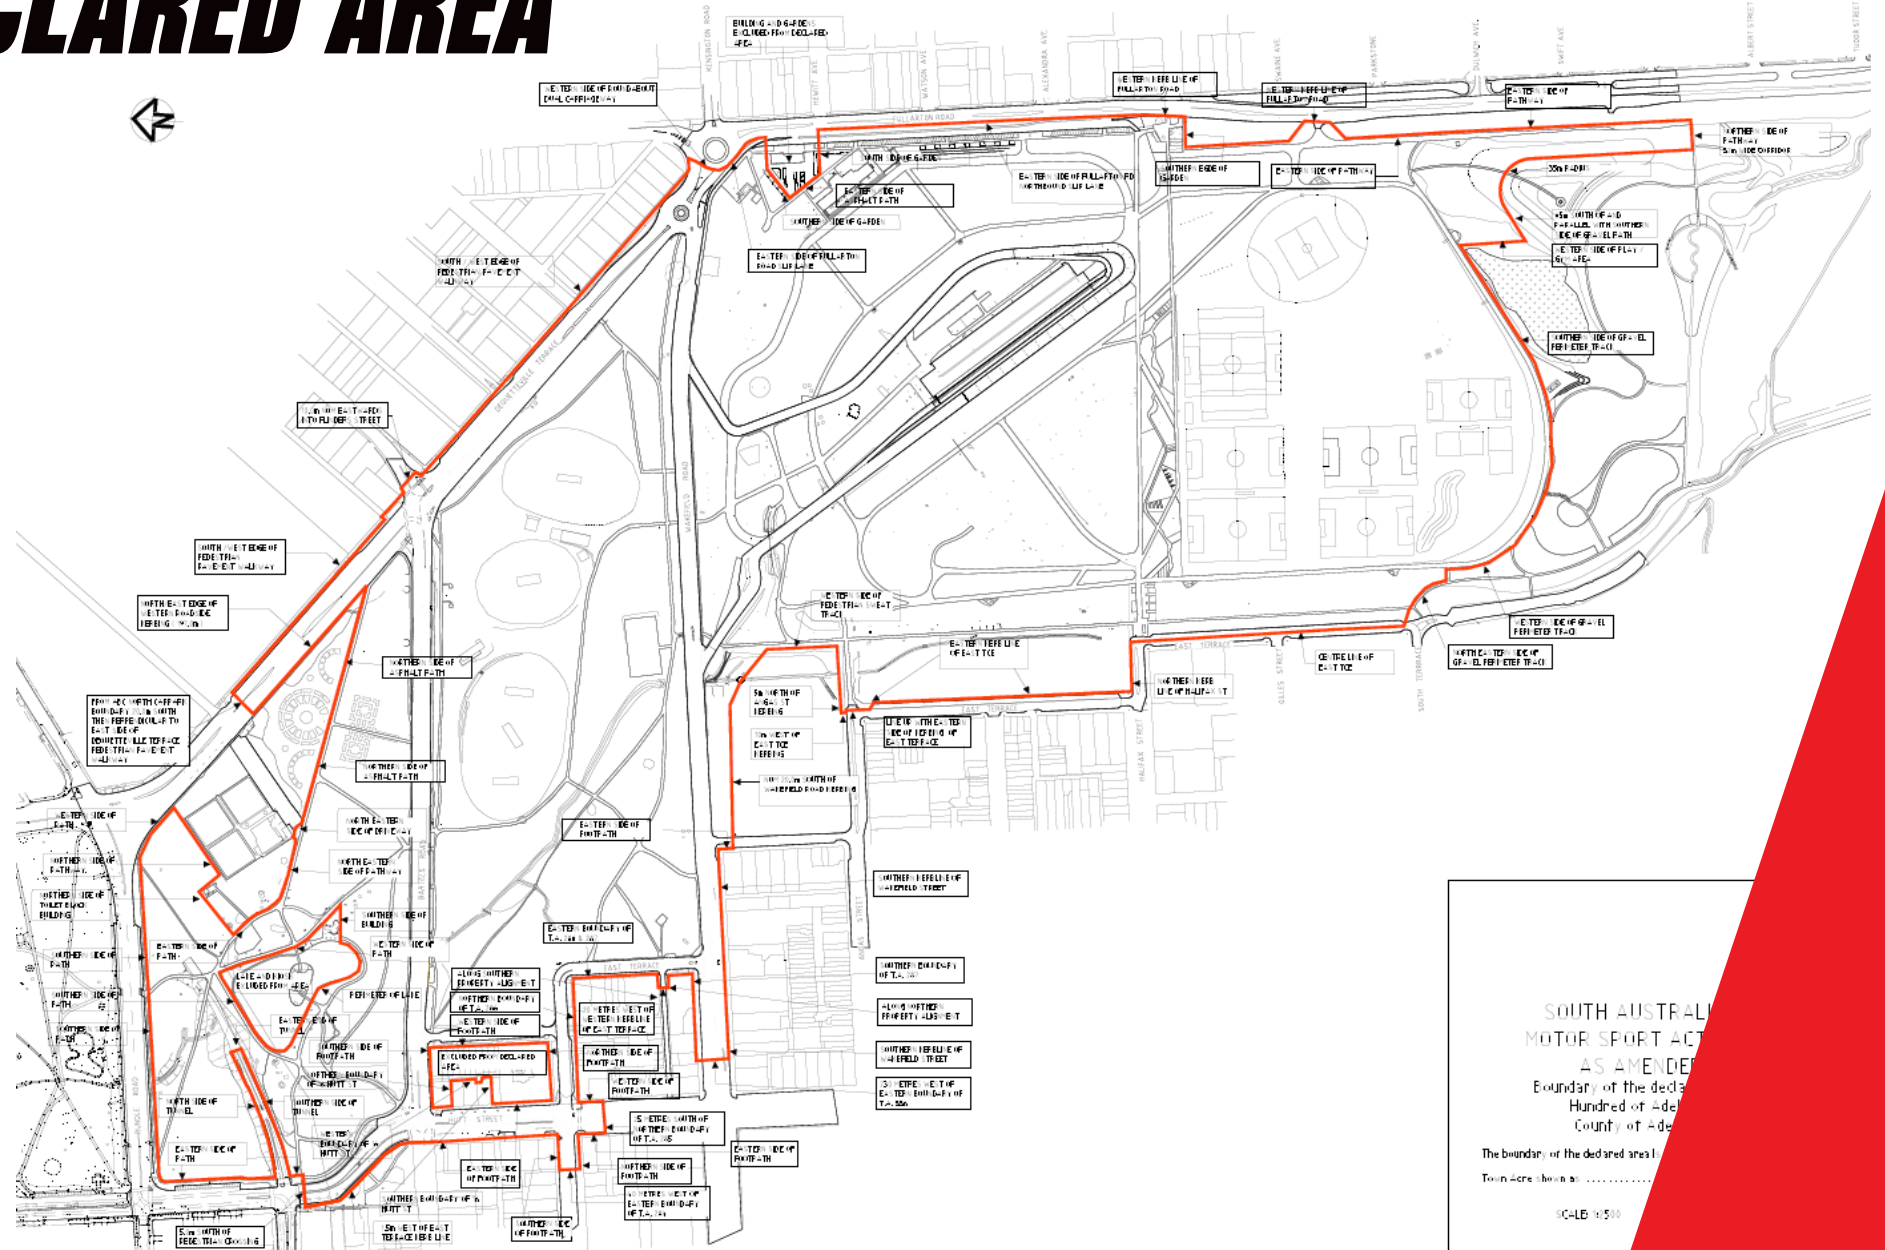

SOUTH AUSTRALIAN
MOTOR SPORT ACT
AS AMENDED
Boundary of the declared
Hundred or Adelaide
County of Adelaide
The boundary of the declared area is
Town here shown as

SCALE 1:500

DATE 15/01/2024

DECLARED AREA CHANGES

– PARK 14

The exclusion of the Quentin Kenihan Inclusive Playspace.

Inclusion of an area within Park 14 between Rymill Lake and Adelaide Bowling Club.


– 16 HUTT ST

Inclusion of the Sofia Restaurant located at 16 Hutt St.

– PARK 16, EAST TCE

Inclusion of parkland between intersections at Angus St and Halifax St along East.

Inclusion of single lane section of East Tce south of Halifax St.

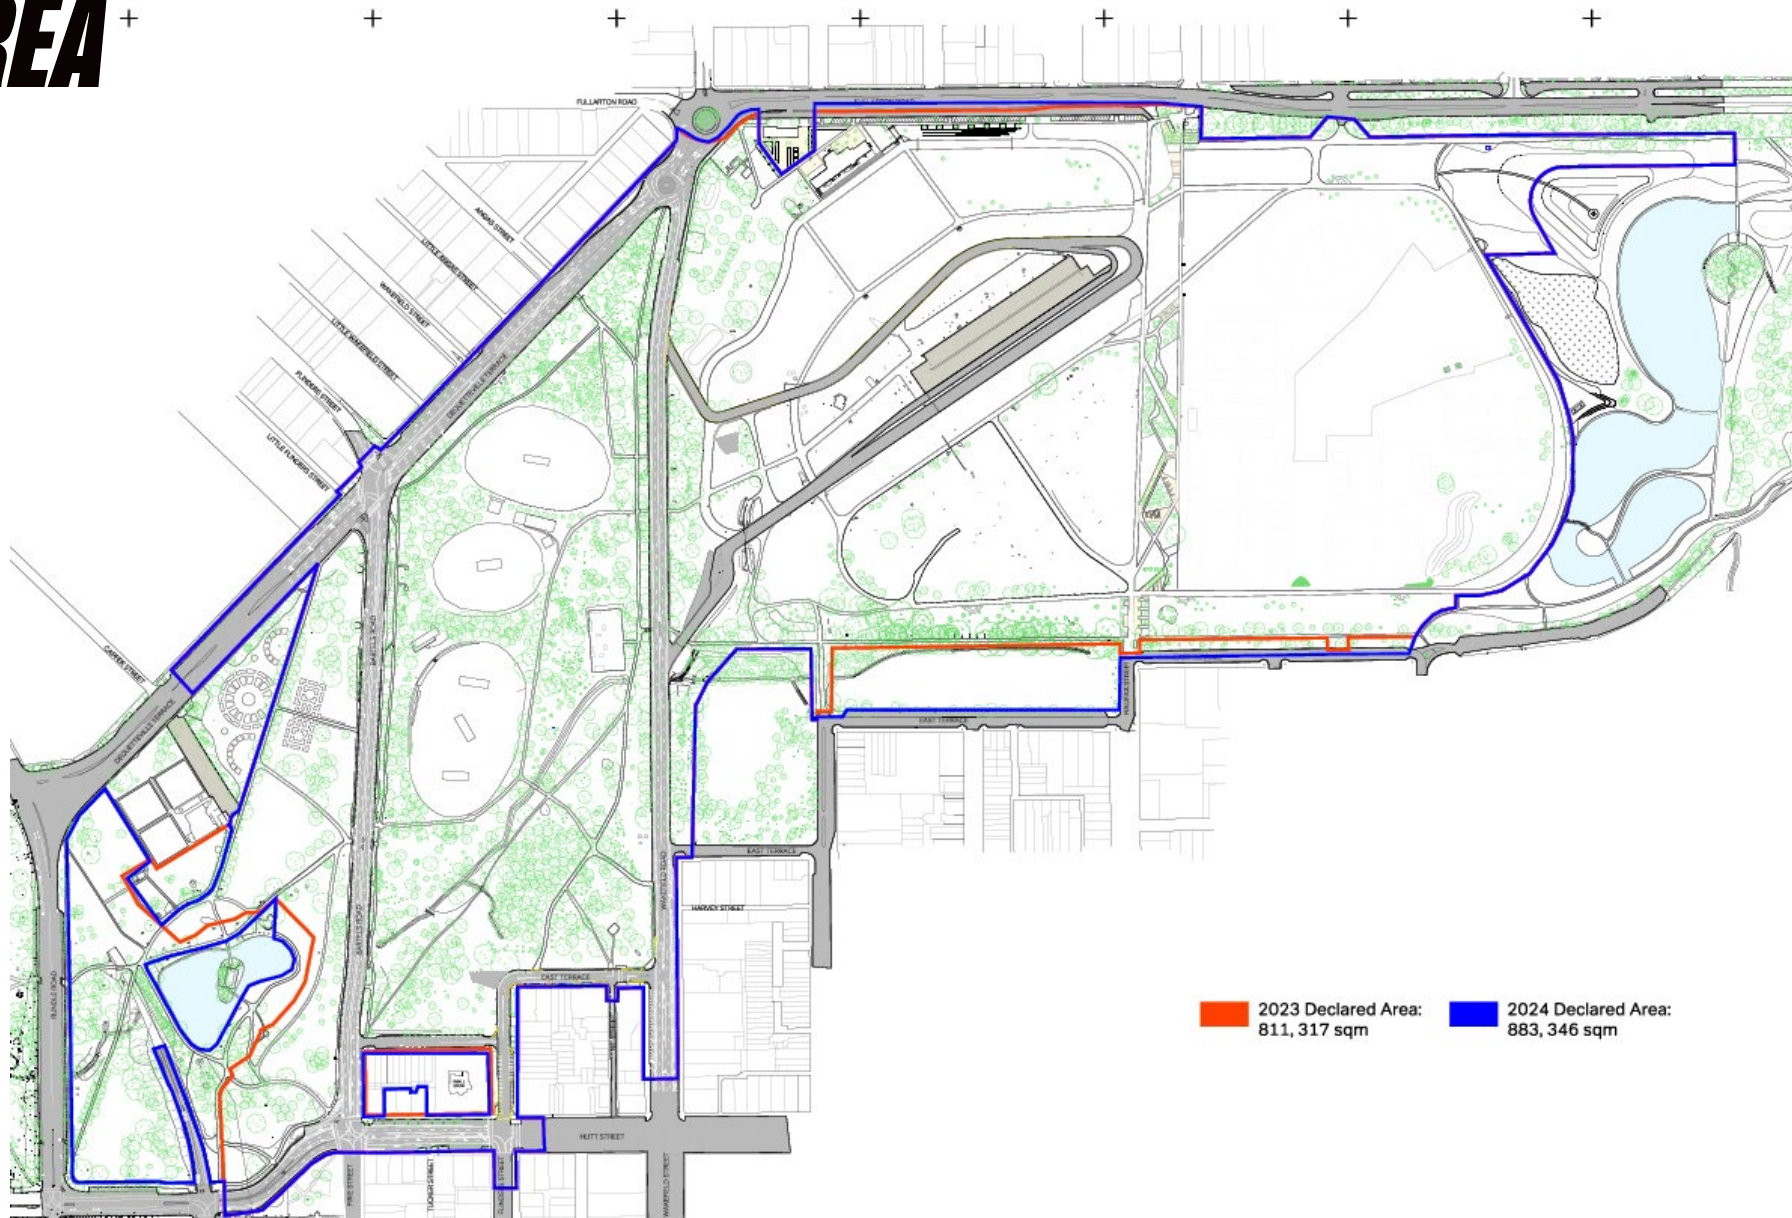

PROGRAM OVERVIEW

19 Aug
2024

Commencement
of Prescribed
Works Period

12 Nov
2024

All Precinct
Roads Closed

13 – 17
Nov
2024

Event
Declared Period

21 Nov
2024

All Precinct
Roads Open


Graduated openings:
Bartels & Hutt – 19 Nov
Dequetteville – 19 Nov
Wakefield – 21 Nov

26 Jan
2025

End of
Prescribed
Works Period

PRESCRIBED WORKS PERIOD & KEY DATES

- Construction will be completed in a phased approach to minimise occupation of parklands where possible
- Handover of parklands will be facilitated with CoA as required to enable the commencement of infrastructure works
- Handback of parklands will be scheduled as soon as dismantle works are complete and areas are cleared to return to open parklands space

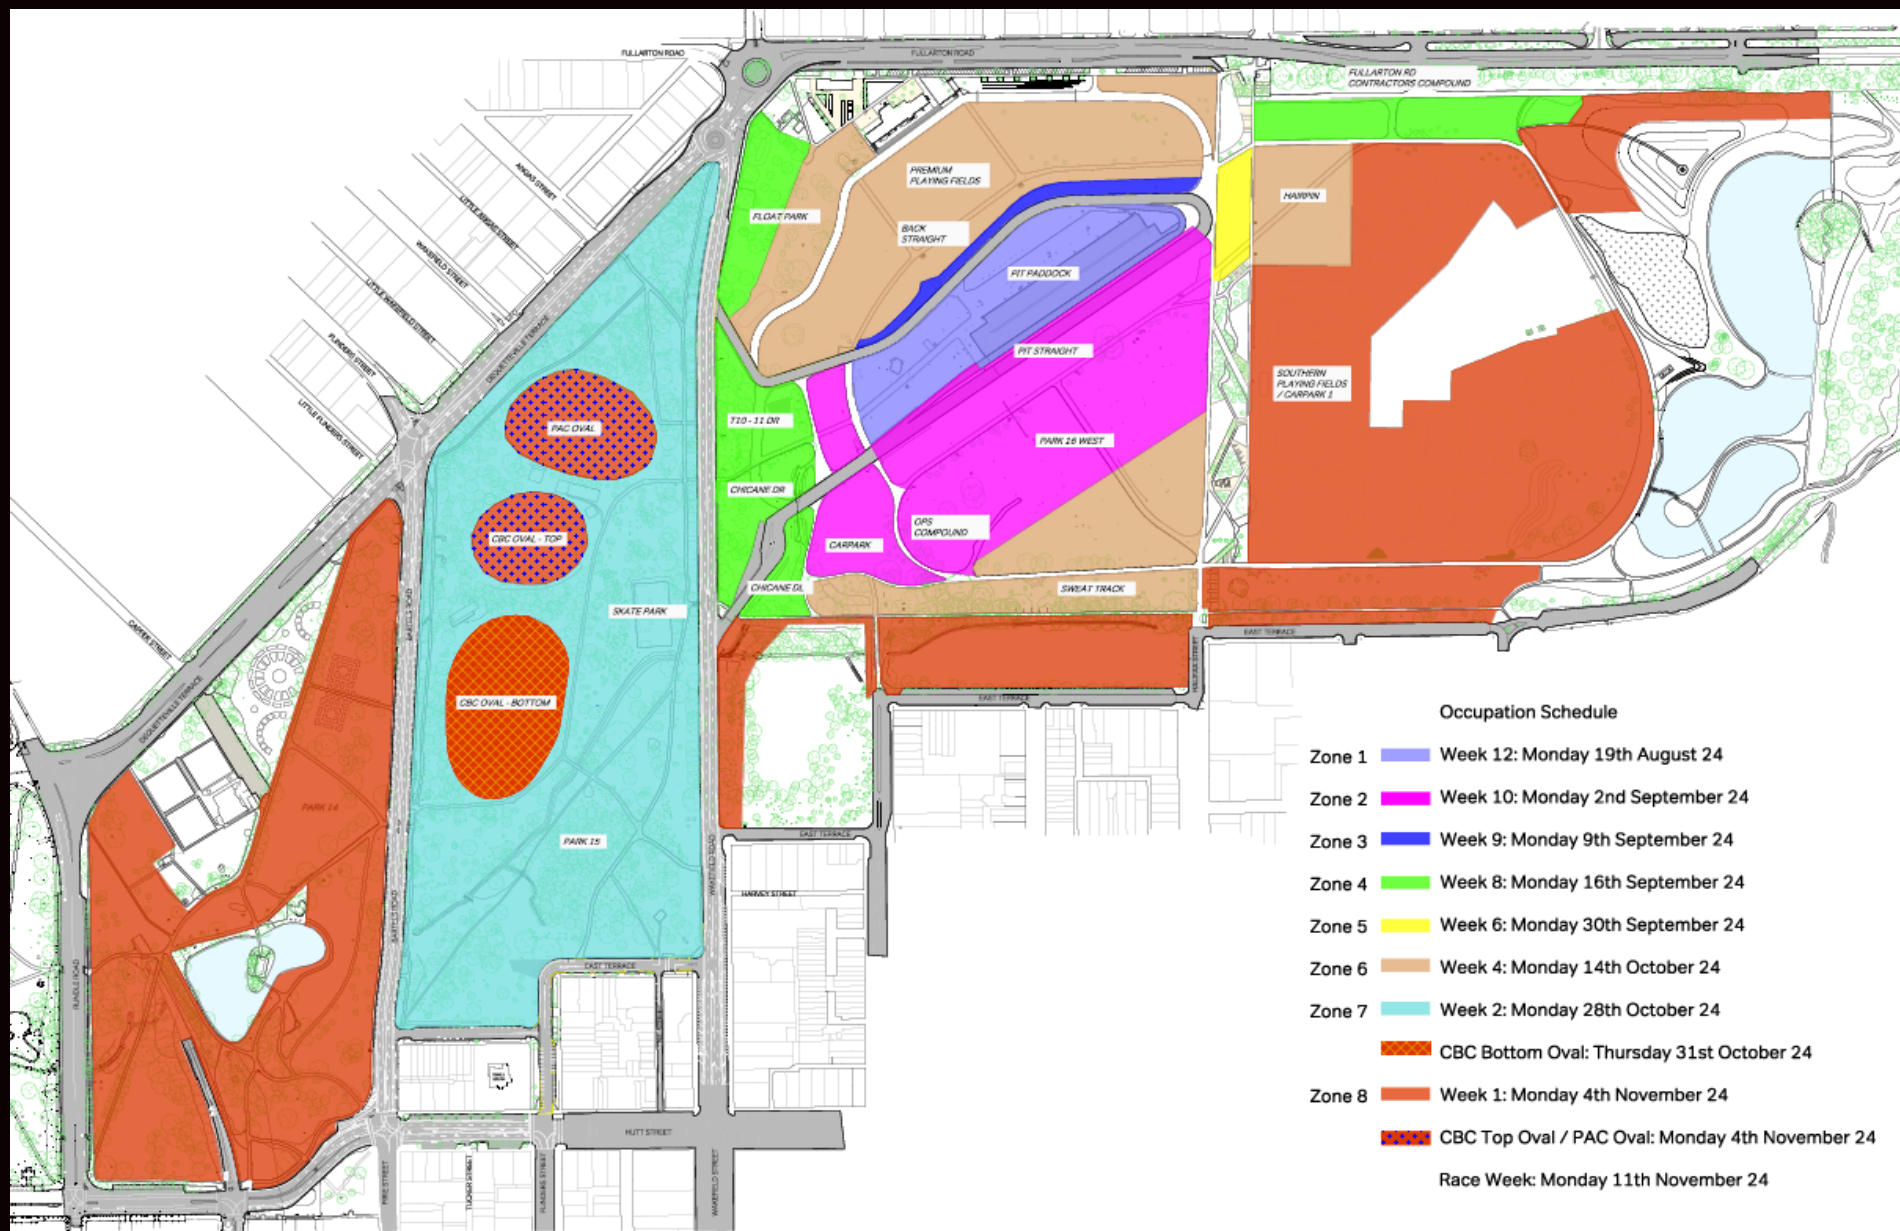


2024 KEY DATES

2024 KEY MILESTONES		FROM	TO	DURATION	2023
PRESCRIBED WORKS PERIOD		Monday 19 August 2024	Sunday 26 January 2025	160	153
ROAD OCCUPATION	Hutt St, Bartels Rd & Dequetteville Tce (North Bartels)	6am Friday 8 November	6am Tuesday 19 November	11	11
	Dequettville Tce (South Bartels)	6am Friday 8 November	3pm Tuesday 19 November	11	11
	Wakefield Rd & East Tce	6am Friday 8 November	6am Thursday 21 November	13	13
E/W FOOTPATHS	Central North E/W	5am Monday 16 September	5pm Sunday 22 December	63	64
	Central South E/W	6am Monday 21 October	5am Monday 2 December	42	42

ROAD CLOSURES

LEGEND

- █ 9am Thursday 31st October 2024 (Hard Closure)
- █ 9am Thursday 7th November 2024 (Hard Closure)
- █ 6am Friday 8th November 2024 (Hard Closure)

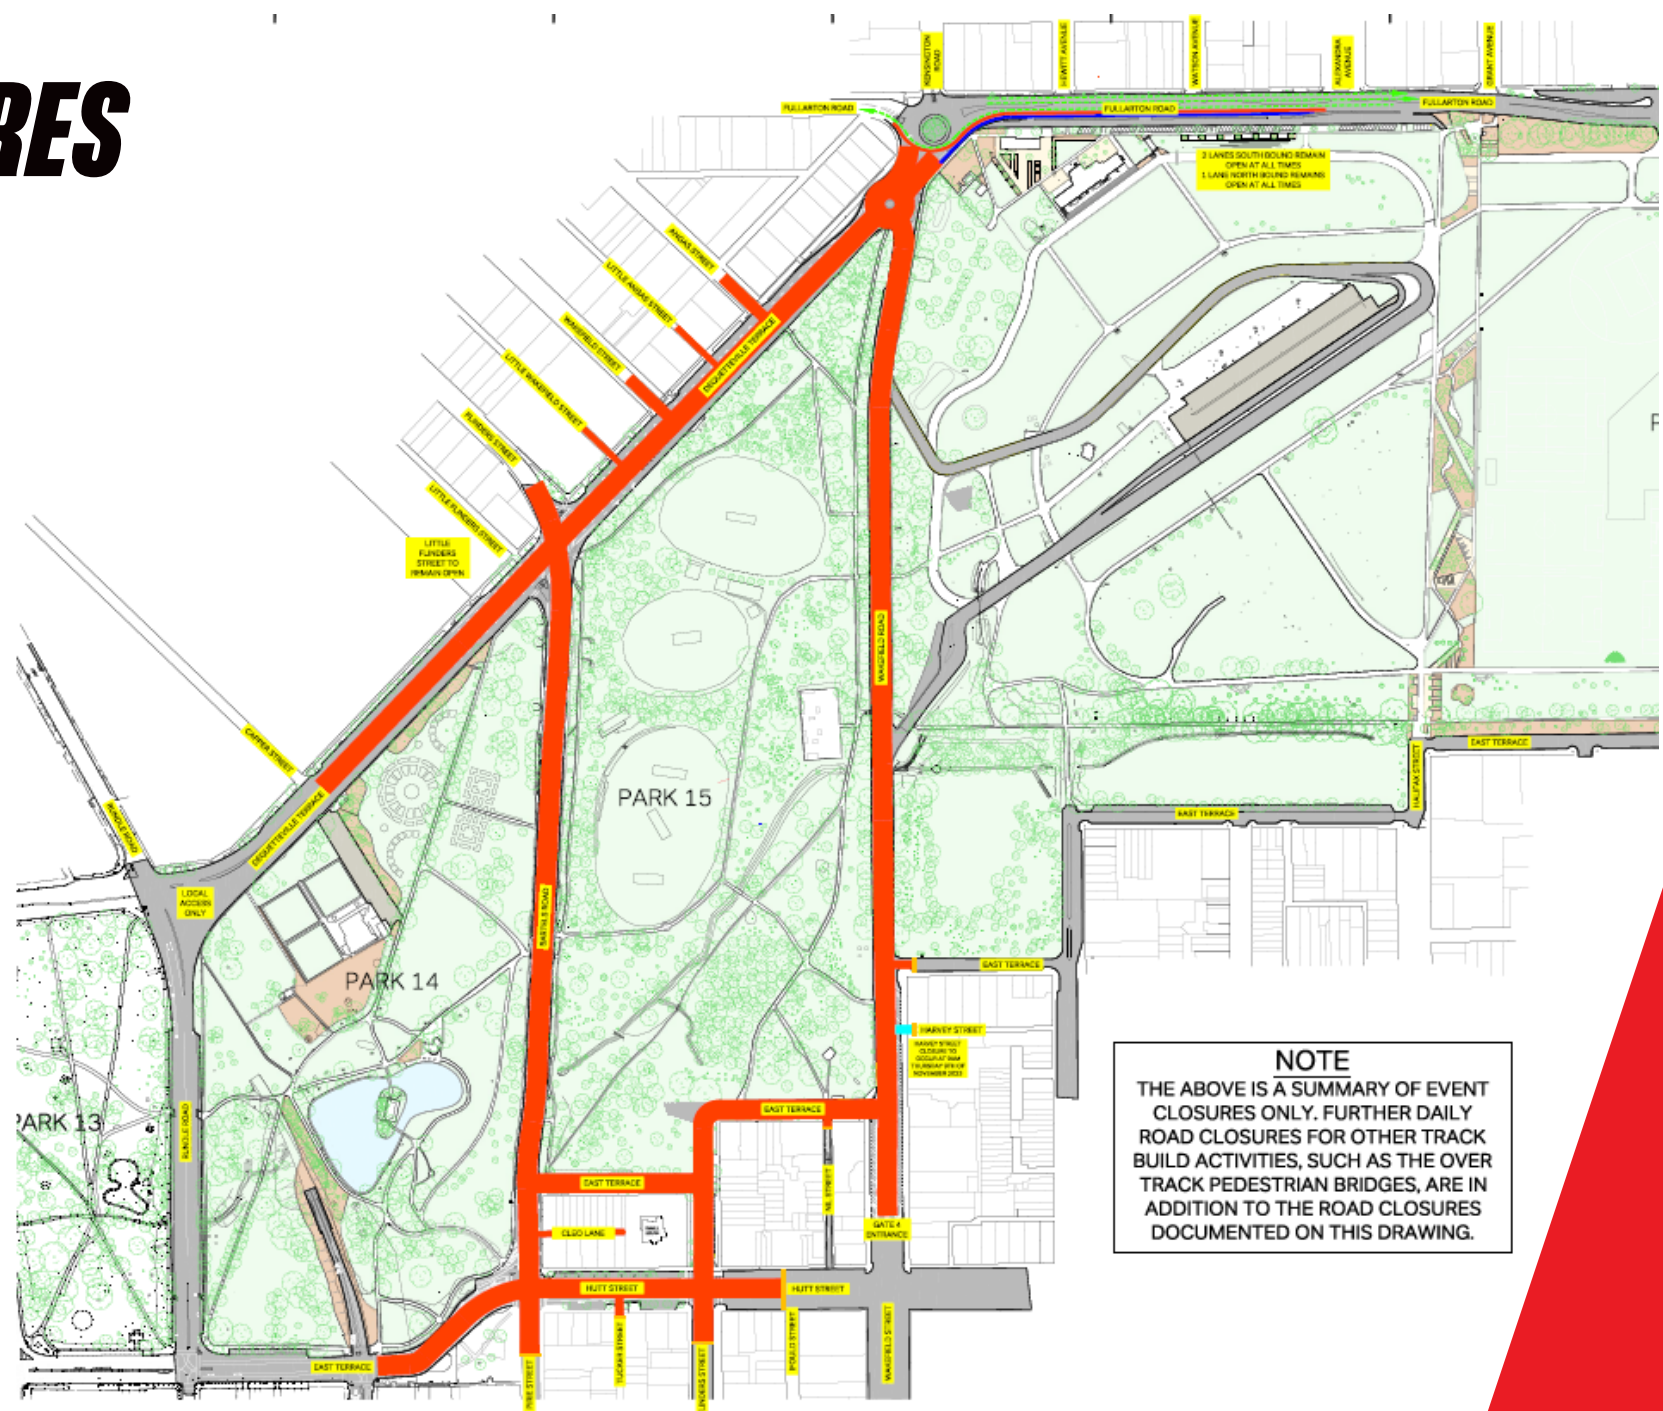


NOTE
 THE ABOVE IS A SUMMARY OF EVENT CLOSURES ONLY. FURTHER DAILY ROAD CLOSURES FOR OTHER TRACK BUILD ACTIVITIES, SUCH AS THE OVER TRACK PEDESTRIAN BRIDGES, ARE IN ADDITION TO THE ROAD CLOSURES DOCUMENTED ON THIS DRAWING.


ROAD OPENINGS

LEGEND

- 6am Tuesday 19th November 2024
- 3pm Tuesday 19th November 2024
- 6am Thursday 21st November 2024

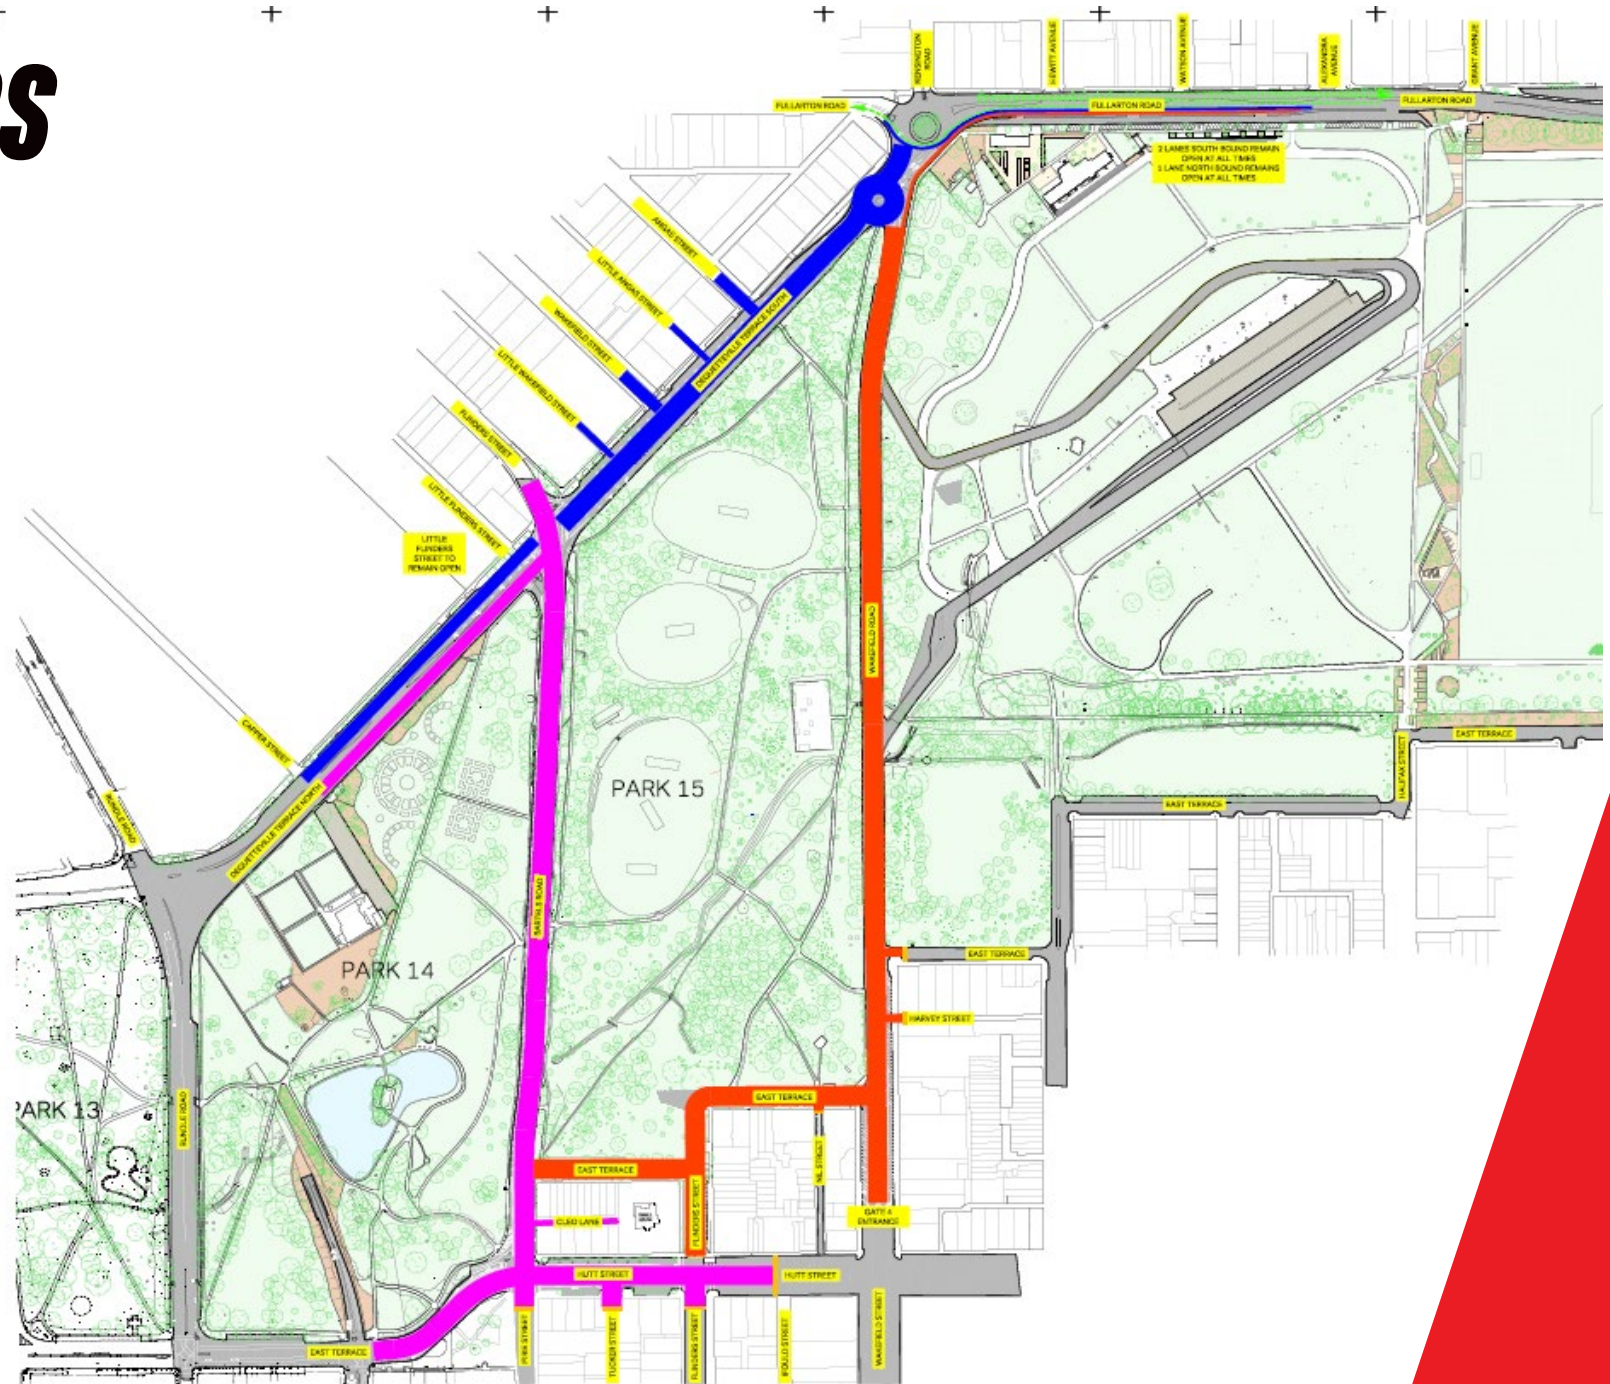

PROPOSED WORKS / IMPROVEMENTS

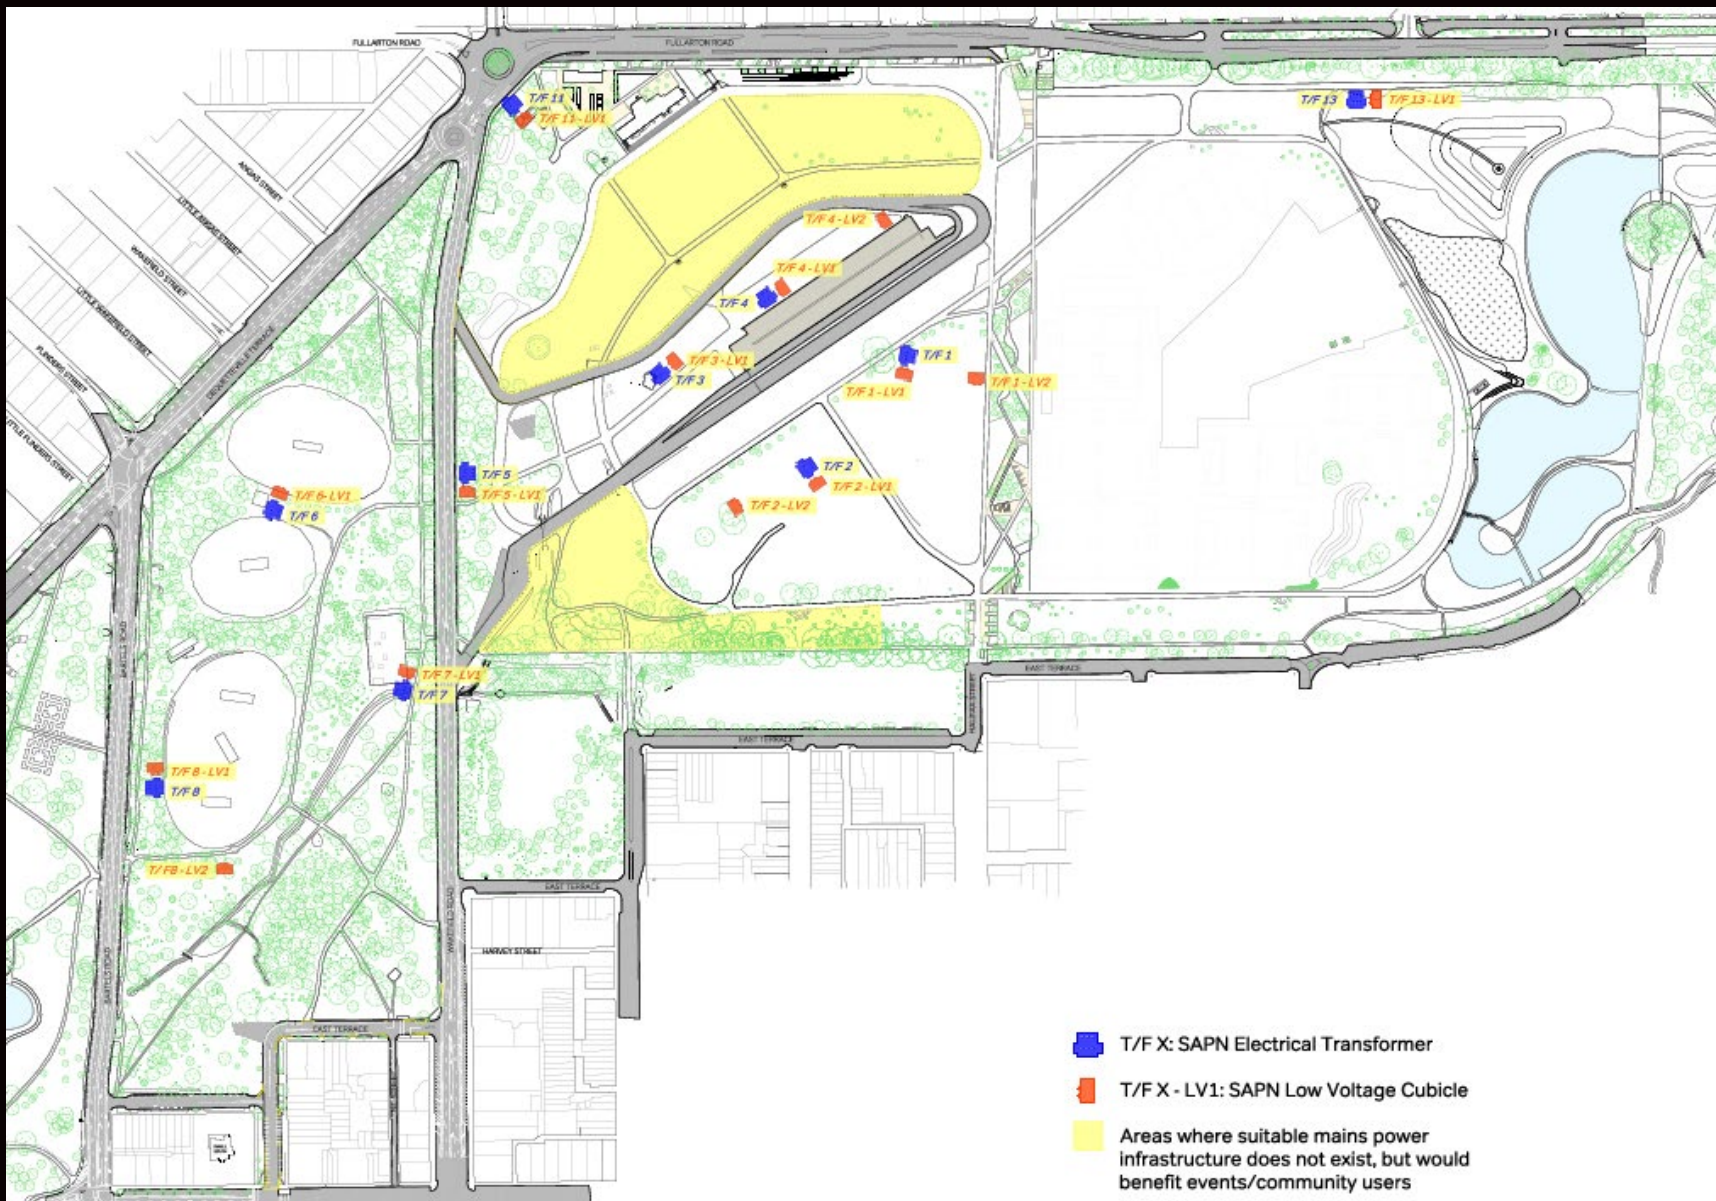

PROPOSED WORKS / IMPROVEMENTS

- The Office of the Technical Regulator (OTR) have advised the electrical infrastructure in Park 15 and Park 16 is non-compliant to the new standards that came into effect in 2023.
- SAPN / City of Adelaide (CoA) have upgraded electrical assets in Park 13 and Park 14 to be compliant for events in those spaces, however not in Park 15 and Park 16.
- Existing SAPN/ City of Adelaide (CoA) LV Cubicles (Park 16) require upgrading to 4 pole switching and to make provisions for all temporary connections required for future events (not just Adelaide 500).
- OTR exemption for non-compliant SAPN/CoA owned permanent infrastructure will be required if upgrades are not completed prior to the 2024 event.
- SAMSB are in process of upgrading its own temporary distribution boards, and will be replacing conduits to ensure compliance to the new regulations

VAILO

ADL

500

14-17 NOV 2024

